Highlands Road Maintenance & Upgrading (Sector) Project
Works Program of Sub Projects under ADB Loan 1709 PNG from October 2001 to December 2009
Revision 2

Project Name	Description	Length km	Contract Price K(M.)	Progress (%)	
Ogulbeng- Mt Ambra	Upgrade	8.85	**4.1**		
			4.47		
Survey,Design &Bid documents				100	Completed
ADB sub project approval				100	Completed
Prequalification and Tender				100	Completed
Contract Award				100	Completed
Construction Works				100	Completed
Ambra - Kotna	Upgrade	15.49	12.59		
			16.27		
Survey,Design &Bid documents				100	Completed
ADB sub project approval				100	Completed
Prequalification and Tender				100	Completed
Contract Signature				100	Completed
Contract Award				100	Completed
Construction Works				100	Completed
Penga-Kotna	**Upgrade**	**4**	5.74		
Possession of Site (FULL)				100	Completed
Construction Works				100	Completed
Mt. Hagen Baiyer (Stage 1)	Upgrade	44.26			
Survey,Design & Bid documents				100	Completed
ADB sub project approval				100	Completed
Prequalification and Tender				100	Completed
Contract Award				100	Completed
Mt Hagen-N.Dame	Rehab.	20.5	**3.5**		
Survey of road corridor				100	Completed
Detailed Design and Bid Document				100	Completed
ADB Review and Approval of Bid Document				100	Completed
Contract Signature				100	Completed
Possesion of Site				100	Completed
Construction Period				58	
N.Dame-Bomb Bridge	Upgrade	13.5	13.7		
BOQ updating &Bid documents				100	Completed
ADB revision & approval				100	Completed
Tender (Post-qualification)				80	
Contract Award				0	
Construction Works				0	
Bomb. Bridge-Baiyer	Upgrade	13.5	12.61		
BOQ updating &Bid documents				100	Completed
ADB revision & approval				100	Completed
Tender (Post-qualification)				80	
Contract Award				0	
Construction Works				0	
Kotna-Banz	Upgrade	33.5	29.6		
Survey of road corridor				100	Completed
Detailed Design and Bid Document				100	Completed
ADB Review and Approval of Bid Document				100	Completed
Contract Signature				100	Completed
Possesion of Site				100	Completed
Construction Period				51	
Kundiawa-Goro	Upgrade	10km	3.8		
			5.94		
Survey,Design &Bid documents				100	Completed
ADB sub project approval				100	Completed
Prequalification and Tender				100	Completed
Contract Signature				100	Completed
Contract Award				100	Completed
Construction Works				100	Completed
Chuave-Move	Rehab.	18.8km	9.4		
			12.9		
Survey of road corridor				100	Completed
Detailed Design and Bid Document				100	Completed
ADB Review and Approval of Bid Document				100	Completed
Contract Signature				100	Completed
Possesion of Site				100	Completed
Construction Period				100	Completed
Goro-Gumine	Upgrade	33.84	27.3		
Survey of road corridor				100	Completed
Detailed Design and Bid Document				100	Completed
ADB Review and Approval of Bid Document				100	Completed
Contract Signature				100	Completed
Possesion of Site				100	Completed
Construction Period				46	
Kundiawa-Gewa	Upgrade	10.6	12		
Survey of road corridor				100	Completed
Detailed Design and Bid Document				100	Completed - TO BE SUBMITTED AFTER THE RESOLUTION OF THE ISSUE OF THE RELOCATION OF THE WATER PIPELINE
ADB BDs approval & Tender				100	Completed - Updated Bid Evaluation Report Submitted
Contract Signature				0	
Possesion of Site				0	
Construction Period				0	NOT YET STARTED (18 MONTHS DURATION)
Kisenapoi - Ialibu	Upgrade	15.6km	11.34		
			15.8		
Survey of road corridor				100	Completed
Detailed Design and Bid Document				100	Completed
ADB Review and Approval of Bid Document				100	Completed
Contract Signature (Original Contract)				100	Completed
Possesion of Site				100	Completed
Construction Period				90	
Contract Signature (New Contract)				100	Completed
Possession of Site				100	Completed
Construction Period				68	

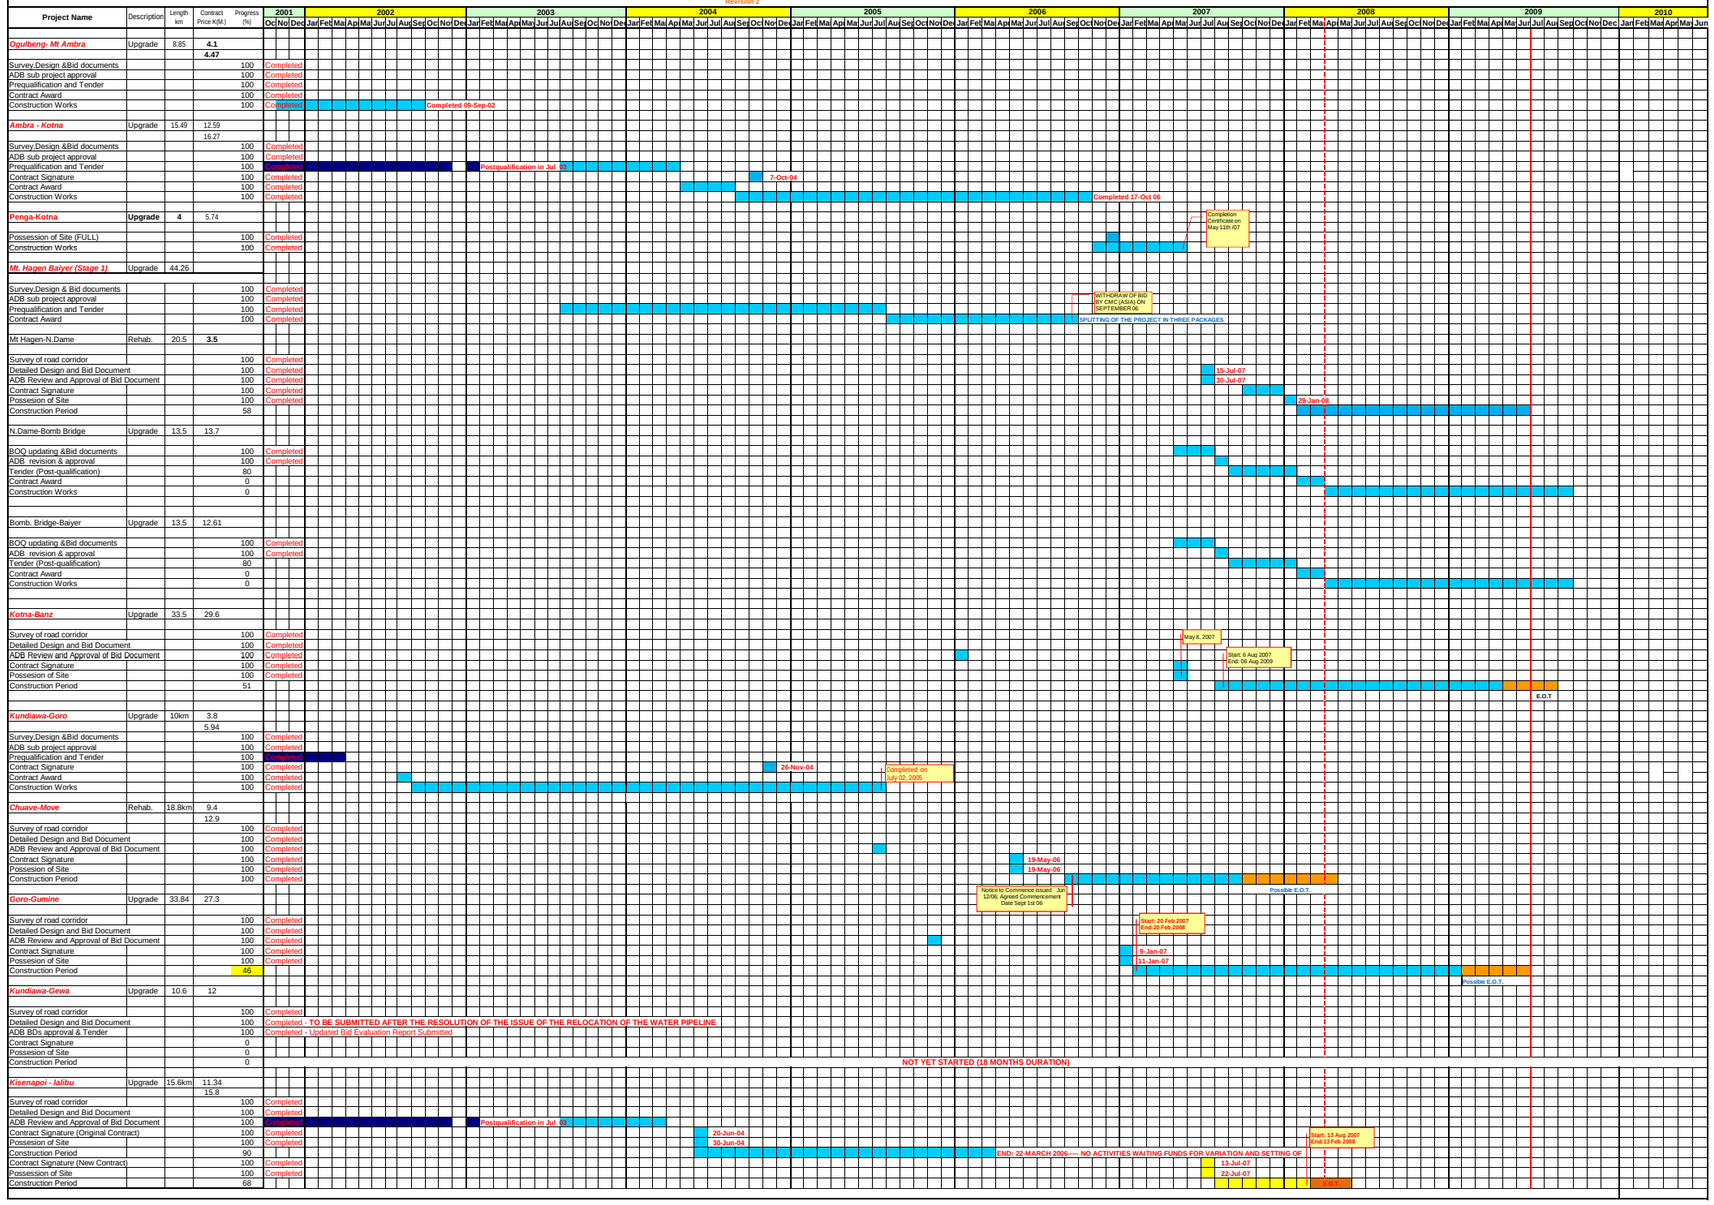
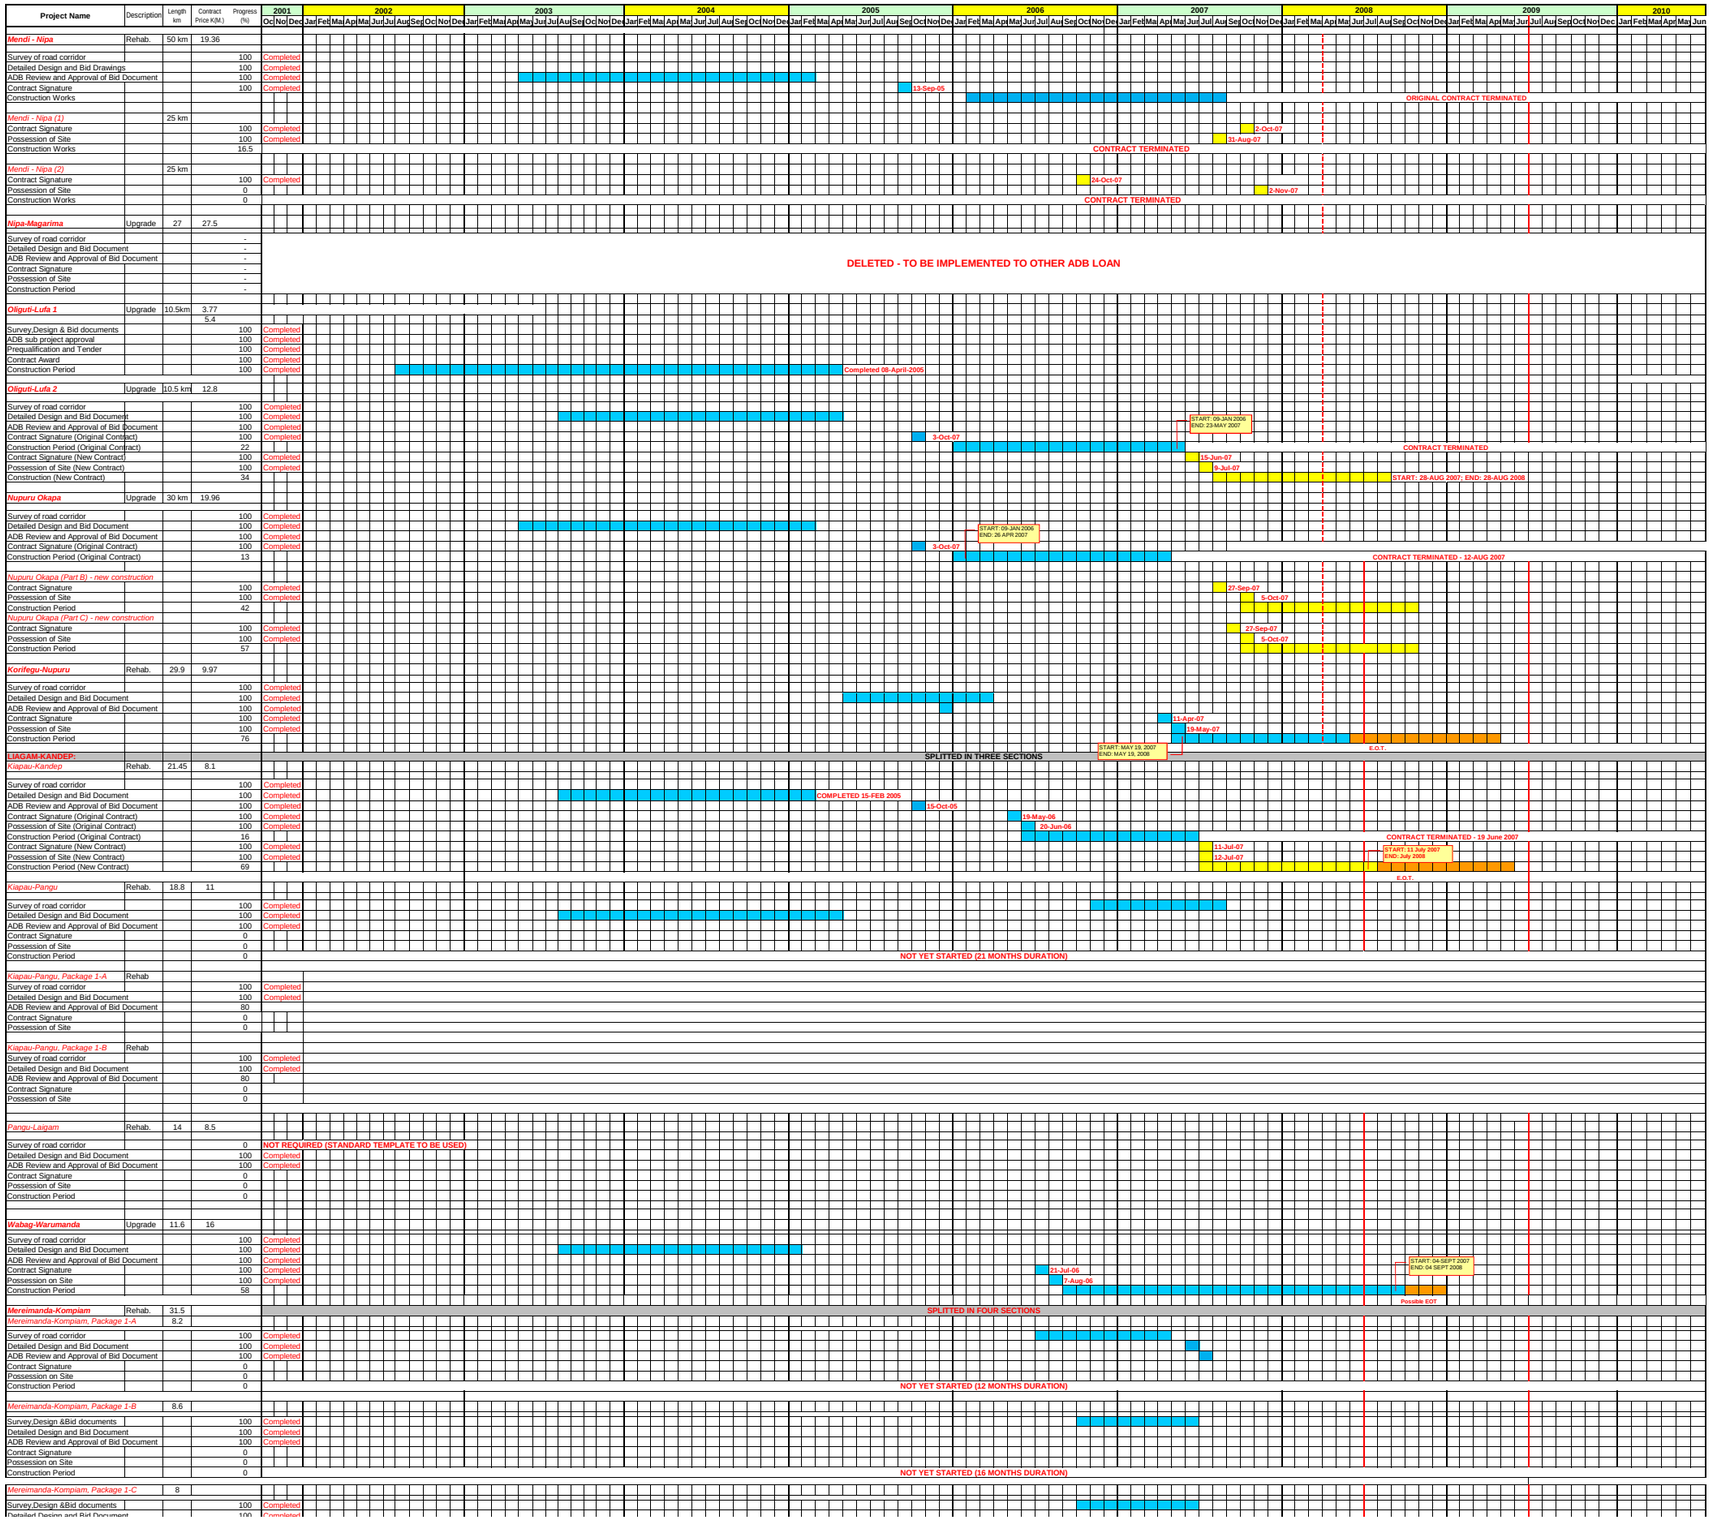
Project Name	Description	Length km	Contract Price K(M)	Progress (%)	
Mendi - Nipa	Rehab.	50 km	19.36		
Survey of road corridor				100	Completed
Detailed Design and Bid Drawings				100	Completed
ADB Review and Approval of Bid Document				100	Completed
Contract Signature				100	Completed
Construction Works					
Mendi - Nipa (1)		25 km			
Contract Signature				100	Completed
Possession of Site				100	Completed
Construction Works				16.5	
Mendi - Nipa (2)		25 km			
Contract Signature				100	Completed
Possession of Site				0	
Construction Works				0	
Nipa-Magarima	Upgrade	27	27.5		
Survey of road corridor				-	
Detailed Design and Bid Document				-	
ADB Review and Approval of Bid Document				-	
Contract Signature				-	
Possession of Site				-	
Construction Period				-	
Oligutl-Lufa 1	Upgrade	10.5km	3.77		
			5.4		
Survey,Design & Bid documents				100	Completed
ADB sub project approval				100	Completed
Prequalification and Tender				100	Completed
Contract Award				100	Completed
Construction Period				100	Completed
Oligutl-Lufa 2	Upgrade	10.5 km	12.8		
Survey of road corridor				100	Completed
Detailed Design and Bid Document				100	Completed
ADB Review and Approval of Bid Document				100	Completed
Contract Signature (Original Contract)				100	Completed
Construction Period (Original Contract)				22	
Contract Signature (New Contract)				100	Completed
Possession of Site (New Contract)				100	Completed
Construction (New Contract)				34	
Nupuru Okapa	Upgrade	30 km	19.96		
Survey of road corridor				100	Completed
Detailed Design and Bid Document				100	Completed
ADB Review and Approval of Bid Document				100	Completed
Contract Signature (Original Contract)				100	Completed
Construction Period (Original Contract)				13	
Nupuru Okapa (Part B) - new construction					
Contract Signature				100	Completed
Possession of Site				100	Completed
Construction Period				42	
Nupuru Okapa (Part C) - new construction					
Contract Signature				100	Completed
Possession of Site				100	Completed
Construction Period				57	
Korifegu-Nupuru	Rehab.	29.9	9.97		
Survey of road corridor				100	Completed
Detailed Design and Bid Document				100	Completed
ADB Review and Approval of Bid Document				100	Completed
Contract Signature				100	Completed
Possession of Site				100	Completed
Construction Period				76	
LAGAM-KANDEP:					
Kapau-Kandep	Rehab.	21.45	8.1		
Survey of road corridor				100	Completed
Detailed Design and Bid Document				100	Completed
ADB Review and Approval of Bid Document				100	Completed
Contract Signature (Original Contract)				100	Completed
Possession of Site (Original Contract)				100	Completed
Construction Period (Original Contract)				16	
Contract Signature (New Contract)				100	Completed
Possession of Site (New Contract)				100	Completed
Construction Period (New Contract)				69	
Kapau-Pangu	Rehab.	18.8	11		
Survey of road corridor				100	Completed
Detailed Design and Bid Document				100	Completed
ADB Review and Approval of Bid Document				100	Completed
Contract Signature				0	
Possession of Site				0	
Construction Period				0	
Kapau-Pangu, Package 1-A	Rehab				
Survey of road corridor				100	Completed
Detailed Design and Bid Document				100	Completed
ADB Review and Approval of Bid Document				80	
Contract Signature				0	
Possession of Site				0	
Kapau-Pangu, Package 1-B	Rehab				
Survey of road corridor				100	Completed
Detailed Design and Bid Document				100	Completed
ADB Review and Approval of Bid Document				80	
Contract Signature				0	
Possession of Site				0	
Pangu-Laigam	Rehab.	14	8.5		
Survey of road corridor				0	NOT REQUIRED (STANDARD TEMPLATE TO BE USED)
Detailed Design and Bid Document				100	Completed
ADB Review and Approval of Bid Document				100	Completed
Contract Signature				0	
Possession of Site				0	
Construction Period				0	
Wabag-Warumanda	Upgrade	11.6	16		
Survey of road corridor				100	Completed
Detailed Design and Bid Document				100	Completed
ADB Review and Approval of Bid Document				100	Completed
Contract Signature				100	Completed
Possession on Site				100	Completed
Construction Period				58	
Mereimanda-Kompiam	Rehab.	31.5			
Mereimanda-Kompiam, Package 1-A		8.2			
Survey of road corridor				100	Completed
Detailed Design and Bid Document				100	Completed
ADB Review and Approval of Bid Document				100	Completed
Contract Signature				0	
Possession on Site				0	
Construction Period				0	
Mereimanda-Kompiam, Package 1-B		8.6			
Survey,Design &Bid documents				100	Completed
Detailed Design and Bid Document				100	Completed
ADB Review and Approval of Bid Document				100	Completed
Contract Signature				0	
Possession on Site				0	
Construction Period				0	
Mereimanda-Kompiam, Package 1-C		8			
Survey,Design &Bid documents				100	Completed
Detailed Design and Bid Document				100	Completed
